

MAJOR INSPECTION CERIFICATE



THIS REPORT COMPLIES WITH RECOGNIZED INTERNATIONAL STANDARDS & TECHNICAL REQUIREMENTS

CLIENT:	HALLIBURTON	REPORT No.:	QC-24-01-TSS-004-NDT MAJ-001
LOCATION:	TSS WORKSHOP & INSPECTION TEST AREA	STANDARD:	ASME SECTION VIII DIV 1 Latest Edition
WORK ORDER #	325816708	SPECIFICATION:	Halliburton Acceptance Criteria H2S STANDARD NACE MQ-01-75 Manufacturing Date Book Specialist Services
DATE:	01-JAN-2024	INSP. DUE DATE:	ANNUAL INSPECTION
TYPE OF INSPECTION:	VISUAL INSPECTION, PRESSURE TEST AND MAGNETIC PARTICLE INSPECTION AND ULTRASONIC THICKNESS GAUGING		

DESCRIPTION:	SURGE TANK VESSEL 50BBL 50PSI	SAP NO.:	11520759
MANUFACTURER:	SPECIALIST SERVICES	SERIAL NO:	FFZ-287
TOP & BOTTOM MINI THICKNESS	6 MM	TOP & BOTTOM CORROSION ALLOWANCE	3 MM
SHELL NOMINAL THICKNESS	8 MM	SHELL CORROSION ALLOWANCE	3 MM

INSPECTION DETAILS

Max. Working Pressure:	50 PSI	Holding Time:	22 Min
Pump S.N.:	13119220 Cal DUE. AUG.2024	Pressure Gauge NO.:	468066 Cal DUE. AUG.2024

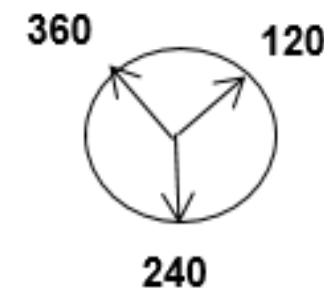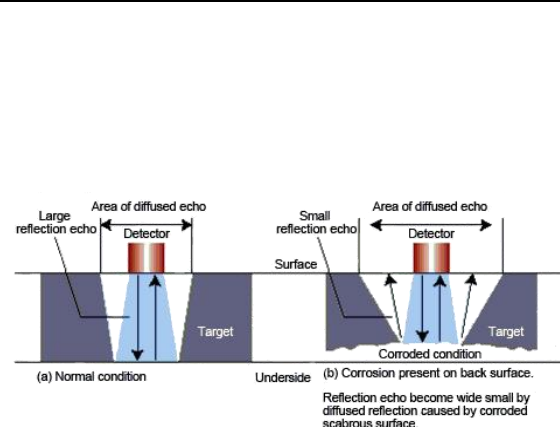

ONLINE TRACEABILITY

A:12'O CLOCK / FORWARD
B:3'O CLOCK / CENTER
C :6'O CLOCK / AFT

* ALL READINGS IN INCH
**MINIMUM THICKNESS PROVIDED BY CUSTMER

ANGLE	THICKNESS AT POSITION			MIN.THICKNESS	FINAL REMARKS
	120°	240°	360°		
SURGE TANK TOP A1	0.391	0.401	0.388	6 MM 0.236 INCH	SATISFACTORY
SURGE TANK TOP A2	0.395	0.405	0.386		
SURGE TANK TOP A3	0.393	0.403	0.395		
SURGE TANK BOTTOM B1	0.392	0.400	0.391		
SURGE TANK BOTTOM B2	0.395	0.405	0.392		
SURGE TANK BOTTOM B3	0.394	0.408	0.398		
SURGE TANK SHELL C	0.361	0.371	0.377	SHELL CORROSION ALLOWANCE 3 MM 0.118 INCH	
SURGE TANK SHELL D	0.369	0.385	0.378		
SURGE TANK SHELL E	0.372	0.379	0.372		
SURGE TANK SHELL F	0.383	0.386	0.384		
SURGE TANK SHELL G	0.372	0.380	0.385		
SURGE TANK SHELL H	0.385	0.383	0.381		

INSPECTION RESULT

VT & MPI	Accepted	* ACCORDING TO ASTM E709(70.94158).
UT	Accepted	According to Halliburton Procedure (H2S STANDERD NACE MQ-01-75) ASME SECTION VIII DIV 1 Latest Edition & Manufacturing Date Book Specialist Services
BODY	Accepted	*** These Are The Actual Readings Need To Follow As Per Halliburton Acceptance Criteria

Inspection Evaluation

(MPI) The Above Item Has No Significant Discontinuous At The Time Of Inspection And Found Acceptable Accordance To The Halliburton Specification ASTM E709 (70.94158)

U.T-The Above Item Was Found Acceptable As Per Halliburton Procedure H2S STANDARD NACE MQ-01-75 ASME SECTION VIII DIV 1 Latest Edition & Manufacturing Date Book Specialist Services

Pressure Test-The Above Item was Pressure Tested 50 PSI Maximum Working pressure Hold On 22 min no Leak was Realized while testing & Pressure Was Stable Accordance To Chart Recorder Attached

INSPECTION EQUIPMENT DETAILS

TECHNICAL DETAILS

AC YOKE S.N:	201504048	CAL DUE DATE	14-Feb-24	White Contrast WCP-2	MANUFACTURE	BATCH NO	EXPIRE DATE
Digital Lux Meter WHITE LIGHT	2722003	CAL DUE DATE	16-Feb-24		Magnaflux	220602	JUN.2025
UT THICKNESS GAUGE:	3997	CAL DUE DATE	16-Feb-24	Black Magnetic Ink 7HF	MANUFACTUR E	BATCH NO	EXPIRE DATE
UT TEST BLOCK:	NoBo5087	CAL DUE DATE	16-Feb-24		Magnaflux	220605	JULY.2025
ASTM Test Block:	1657	CAL DUE DATE	14-Feb-24	Fluorescent Magnetic Ink 7HF	1.2 to 2.4 ml/100 ml		
WHITE LIGHT INTENSITY:	3630 lux						

PERSON DETAILS

INSPECTOR NAME:	M.Shanzad Ahmed	SENIOR INSPECTOR:	NAVEED HUSSAIN	CLIENT:	
QUALIFICATION:	ASNT CP	INSPECTION SUPERVISOR:	HANI ALI	HB&SIGN	
SIGNATURE & STAMP:				DATE:	

Original - Client Files Copy - Area Office QC/IN/PT/077 Rev.00 DATED 07.NOV. 2021

