
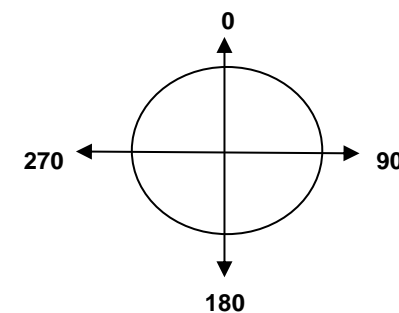
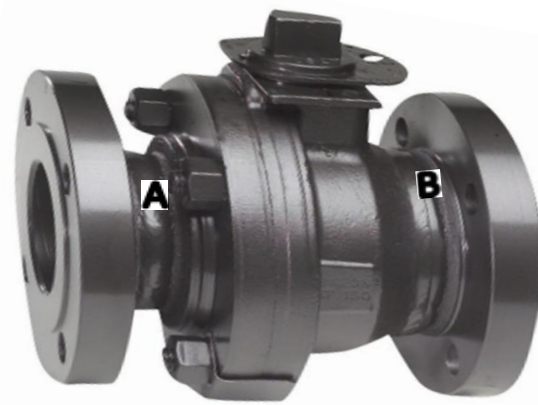


## MAJOR INSPECTION CERIFICATE

THIS REPORT COMPLIES WITH RECOGNIZED INTERNATIONAL STANDARDS & TECHNICAL REQUIREMENTS

CLIENT:	<b>HALLIBURTON</b>	REPORT No.:	QC-24-01-TSS-004-NDT MAJ-005
LOCATION:	TSS WORKSHOP & INSPECTION TEST AREA	STANDARD:	ASME SECTION VIII DIV 1 Latest Edition
WORK ORDER #	325816708	SPECIFICATION:	Halliburton Acceptance Criteria H2S STANDARD NACE MQ-01-75 Manufacturing Date Book Specialist Services
DATE:	01-JAN-2024	INSP. DUE DATE:	<b>ANNUAL INSPECTION</b>
TYPE OF INSPECTION:	VISUAL INSPECTION, PRESSURE TEST AND MAGNETIC PARTICLE INSPECTION AND ULTRASONIC THICKNESS GAUGING		

DESCRIPTION:	4" BALON VALVE	SAP NO.:	11520759
MANUFACTURER:	SPECIALIST SERVICES	SERIAL NO.:	3GZN
<b>INSPECTION DETAILS</b>			
Max. Working Pressure:	50 PSI	Holding Time:	22 Min
Pump S.N.:	13119220 Cal DUE. AUG.2024	Pressure Gauge NO.:	468066 Cal DUE. AUG.2024



ONLINE TRACEABILITY

A: 12'O CLOCK / FORWARD  
B: 3'O CLOCK / CENTER  
C: 6'O CLOCK / AFT  
  
\* ALL READINGS IN INCH  
\*\*MINIMUM THICKNESS PROVIDED BY CUSTMER

ANGLE	THICKNESS AT POSITION				NOMINAL THICKNESS	FINAL REMARKS
	0°	90°	180°	270°		
A	0.457	0.444	0.435	0.446	7.62 MM 0.300 INCH	SATISFACTORY
B	0.487	0.439	0.438	0.451		

INSPECTION RESULT		
VT & MPI	Accepted	* ACCORDING TO ASTM E709(70.94158).
UT	Accepted	According to Halliburton Procedure (H2S STANDERD NACE MQ-01-75) ASME SECTION VIII DIV 1 Latest Edition & Manufacturing Date Book Specialist Services
BODY	Accepted	*** These Are The Actual Readings Need To Follow As Per Halliburton Acceptance Criteria

**Inspection Evaluation**

(MPI) The Above Item Has No Significant Discontinuous At The Time Of Inspection And Found Acceptable Accordance To The Halliburton Specification ASTM E709 (70.94158)

U.T-The Above Item Was Found Acceptable As Per Halliburton Procedure H2S STANDARD NACE MQ-01-75 ASME SECTION VIII DIV 1 Latest Edition & Manufacturing Date Book Specialist Services

Pressure Test-The Above Item was Pressure Tested 50 PSI Maximum Working pressure Hold On 22 min no Leak was Realized while testing & Pressure Was Stable Accordance To Chart Recorder Attached

INSPECTION EQUIPMENT DETAILS				TECHNICAL DETAILS			
AC YOKE S.N:	201504048	CAL DUE DATE	14-Feb-24	White Contrast WCP-2	MANUFACTURE	BATCH NO	EXPIRE DATE
Digital Lux Meter WHITE LIGHT	2722003	CAL DUE DATE	16-Feb-24		Magnaflux	220602	JUN.2025
UT THICKNESS GAUGE:	3997	CAL DUE DATE	16-Feb-24	Black Magnetic Ink 7HF	MANUFACTURE	BATCH NO	EXPIRE DATE
UT TEST BLOCK:	NoBo5087	CAL DUE DATE	16-Feb-24		Magnaflux	220605	JULY.2025
ASTM Test Block:	1657	CAL DUE DATE	14-Feb-24	Fluorescent Magnetic Ink 7HF		1.2 to 2.4 ml/100 ml	
WHITE LIGHT INTENSITY:	3630 lux						

PERSON DETAILS			
INSPECTOR NAME:	M.Shahzad Ahmed	SENIOR INSPECTOR:	NAVEED HUSSAIN
QUALIFICATION:	ASNT CP	INSPECTION SUPERVISOR:	HANI ALI
SIGNATURE & STAMP:			DATE:

Original - Client Files Copy - Area Office QC/FN/PT/077 Rev.00 DATED 07.NOV. 2021

