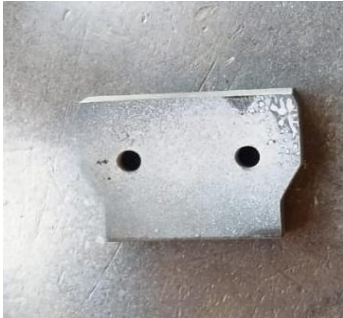




### CERTIFICATION OF VISUAL, THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION

<b>Client:</b>	HALLIBURTON (WPS)	<b>Report No:</b>	QC/24/HALL-WPS-FEB-011	
<b>Location:</b>	WPS YARD	<b>Job Number:</b>	QC-24/HALL-WPS-003	
<b>Inspection Date:</b>	Tuesday, February 27, 2024	<b>Next Inspection Date:</b>	Monday, August 26, 2024	
<b>Type Of Inspection:</b>	VISUAL , THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION		<b>Specification:</b> ASTM E709 & ASTM E 1444 (2016) ASME V Article 7 (2019)	
		<b>UNIT DESCRIPTION:</b>	SHEAR BLADE 3" EC LOWER	
		<b>PART NO:</b>	L-9701072597	
		<b>UNIT S/N:</b>	006522-2	
		<b>INSPECTION RESULT :</b>		
		VISUAL , THOROUGH EXAMINATION	unit fully inspected and found free from deforms, cracks, corrosion & mechanical damage	
		MAGNETIC PARTICLE INSPECTION	Full Body areas inspected and found free from cracks and other defects	
		FINAL RESULTS	unit found satisfactory and free of defects at the time of inspection	
<b>COMMENT:</b>				
Magnetic Particle Inspection With A/C Hand Yoke , Black & White Contrast				
<b>EQUIPMENT DETAILS</b>				
<b>Equipment:</b>	AC-Yoke Test Block	<b>Equipment:</b>	Digital Lux Meter	
<b>S.No:</b>	1657	<b>S.No:</b>	2722003	
<b>Cal Due Date:</b>	12-Aug-24	<b>Cal Due Date:</b>	14-Aug-24	
<b>Black Magnetic Ink Manufacture:</b>	Magnaflux	<b>Batch No:</b>	220605	
<b>Whie Contrast Paint Manufacture:</b>	Magnaflux	<b>Batch No:</b>	220602	
<b>Equipment:</b>	AC/DC Yoke	<b>Expiry Date:</b>	JULY.2025	
<b>Technical Details:</b>	<b>Magnetic Partical Concentration</b>	<b>Method</b>	<b>WMPT Light Intensity</b>	
	1.2 to 2.4 ml/100 ml	Wet Magnetic Particle Testing (WMPT)	3560 Lux	
Original - Client Files		Copy - Area Office		
QC/FN/MPI/065 Rev.00 DATED 07 NOV 2021				
<b>PERSON DETAILS</b>				
<b>INSPECTOR NAME:</b>	M.SHAHZAD AHMED		<b>SENIOR INSPECTOR:</b>	NAVEED HUSSAIN
<b>QUALIFICATION:</b>	ASNT LEVEL II MT & PT & VT		<b>SUPERVISOR:</b>	HANI ALI
<b>STAMP &amp; SIGNATURE:</b>			<b>CLIENT:</b>	
