# Al TAKAMUL COMPANY FOR ENGINEERING TESTS AND PROFESSIONAL SAFETY LIMITED



# Basra, North Rumaila, Quality Control Yard - Iraq

## CERTIFICATION OF VISUAL, THOROUGH EXAMINATON & MAGNETIC PARTICLE INSPECTION

Client:	HALLIBURTON (HPS)	Report No:	QC/24/HALL-HPS-APRIL-001A
Location:	HPS YARD	Job Number:	QC-24/HALL-HPS-001
Date:	Tuesday, April 16, 2024	Next Inspection Date:	Tuesday, October 15, 2024
Type Of Inspection:	VISUAL , THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION	Specification:	ASTM E709 & ASTM E 1444 (2016) ASME V Article 7 (2019)







UNIT DESCRIPTION:	FRAC TANK LIFTING LUGS				
UNIT S/N:	12128624				
UNIT DIM:	13.50 M (L) X 2.60 M (W) X 3.65 M (H)				
INSPECTION RESULT :					
VISUAL , THOROUGH EXAMINATION	unit fully inspected and found free from				

deforms, cracks, corrosion & mechanical damage Welds & forgn areas inspected **MAGNETIC PARTICLE INSPECTION** and found free from cracks and other defects unit found satisfactory and free of defects **FINAL RESULTS** at the time of inspection

#### COMMENT:

Magnetic Particle Inspection With A/C Hand Yoke, Black & White Contrast

EQUIPMENT DETAILS						PERSON DETAILS		REVIEW BY			
Equipment:	AC-Yoke Test	t Block	Equipment:	Digital Lux	Meter	Equipmen	AC/DC Yoke	INSPECTOR NAME: Usman Shabbir	1 Corps	SENIOR INSPECTOR:	ASHRAF ELSAID
S.No:	1657		S.No:	272200	)3	S.No:	201504052				
Cal Due Date:	12-Aug-2	24	Cal Due Date:	14-Aug	24	Cal Due Da	e: 12-Aug-24	QUALIFICATION	10/104	SUPERVISOR:	HANI ALI
Black Magnetic	c Ink Manufac	ture:	Magnaflux	Batch No:	2206	05 Expiry	Date: JULY.2025	ASNT LEVEL II			
Whie Contrast Paint Manufacture:		ture:	Magnaflux	Batch No:	2206	02 Expiry	Date: JUN,2025	MT & PT & VT			
Technical Details:		Magnet	tic Partical Concent	ration	Meth	hod WMPT Light Intensity		STAMP &	or Ingineering	CLIENT:	
		1.2 to 2.4 ml/100 ml		Wet N	Wet Magnetic Particle Testing (WMPT)		3630 Lux	SIGNATURE:	7		

Original - Client Files

Copy - Area Office

QC/FN/MPI/065 Rev.00 DATED 07 Nov 2021





















### AI TAKAMUL COMPANY FOR ENGINEERING TESTS AND PROFESSIONAL SAFETY LIMITED




Basra, North Rumaila, Quality Control Yard - Iraq

### CERTIFICATE OF QUALIFICATION VISUAL INSPECTION AND LEAK TESTING

THIS REPORT COMPLIES WITH RECOGNIZED INTERNATIONAL STANDARDS & TECHNICAL REQUIEREMENTS

CLIENT:	HALLIBURTON (HPS)						
LOCATION:	HPS YARD	REPORT No.:	QC-24-HALL-HPS-April- VT & LEAK -001B				
STANDARD:	CUSOMER SPECIFICATION	JOB NO:	QC-24/HALL-HPS-001				
INSPECTION DATE:	Tuesday, April 16, 2024	Due Date	Tuesday, October 15, 2024				
TYPE OF INSPECTION:	*VISUAL TESTING AND *LEAK TESTING						
DESCRIPTION: FRAC TANK		SAP NO:	12128624				
MEDIUM USED: WATER		HOLDING TIME:	15 MINUTES				
PICTURES							



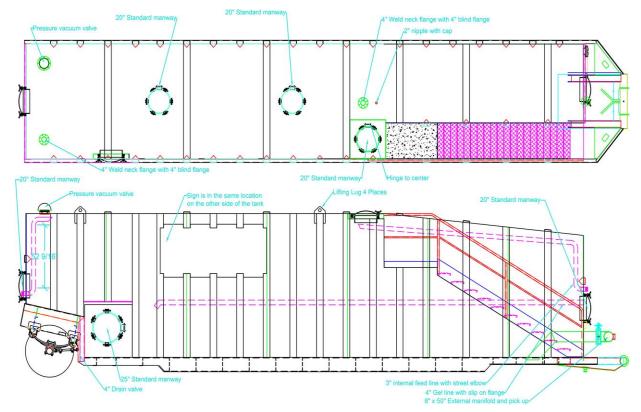

### INSPECTION RESULT

VISUAL TESTING:	Visual Testing of Frac Tank did not found Deforms Mechanical Damage, Cracks and Corrosion. At time of Inspection.			
LEAK TESTING:	Leak Testing of Frac Tank did not found any leakage during the holding time. At time of Inspection.			

#### **Inspection Evaluation**

VISUAL TESTING-The above mentioned Frac Tank was found "Satisfactory" Fit for intended used.

**LEAK TESTING**- The above mentioned Frac Tank was found "Satisfactory" Fit for intended used.

PERSONNEL DETAILS			REVIEW BY			
NAME:	Usman Shabbir	Samu Compani	SENIOR INSPECTOR:	ASHRAF ELSAID	CUSTOMER NAME	
QUALIFICATION:	ASNT LEVEL II MT,PT,VT		SUPERVISOR:	HANI ALI		
STAMP & SIGNATURE:		DATE:				
Original - Client Files Copy - Area Office QC/FN/MPI/065 Rev.00 DATED 07 NOV 2021						





















Tel: +9647810009138 / +9647834964657 Email: OP@qualitycontrol-iraq.com hany.akafi@qualitycontrol-iraq.com
