Al TAKAMUL COMPANY FOR ENGINEERING TESTS AND PROFESSIONAL SAFETY LIMITED






THE ABOVE INSPECTED AREAS WAS ACCEPTED

CERTIFICATION OF VISUAL, THOROUGH EXAMINATON & MAGNETIC PARTICLE INSPECTION				
Client:	HALLIBURTON (HPS)	Report No:	QC-24-04-HPS-NDT-004	
Location:	HPS YARD	JOB NO:	QC-HPS-17-04-24	
Inspection Date:	Wednesday, April 17, 2024	Next Inspection Date:	Wednesday, October 16, 2024	
Type Of Inspection:	VISUAL , THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION	Specification:	DS-1 Volume 4 Fifth Edition,	
		Halliburton Doc.	(Visual Procedure D00305796 Revision U) (MPI Procedure D00976850 Revision D)	
		UNIT DESCRIPTION:	1.75" MHA 1-1/4 AMMT PIN X BOX CONNECTION	
		Serial Number	P060B4124-12-3	
		INSPECTION RESULT :		
		VISUAL, THOROUGH EXAMINATION		AL & MAGNETIC PARTICLE INSPECTION (M.P.I.) HAD BEEN DONEON THE AVAILABLE AREAS FOR THE ABOVE DESCRIPTION
		MAGNETIC PARTICLE INSPECTION		Thread &Body areas inspected and found free from cracks and other defects

COMMENT:

(MPI Wet Fluorescent inspection Thread & Body With UltraViolet Light)

FINAL RESULTS

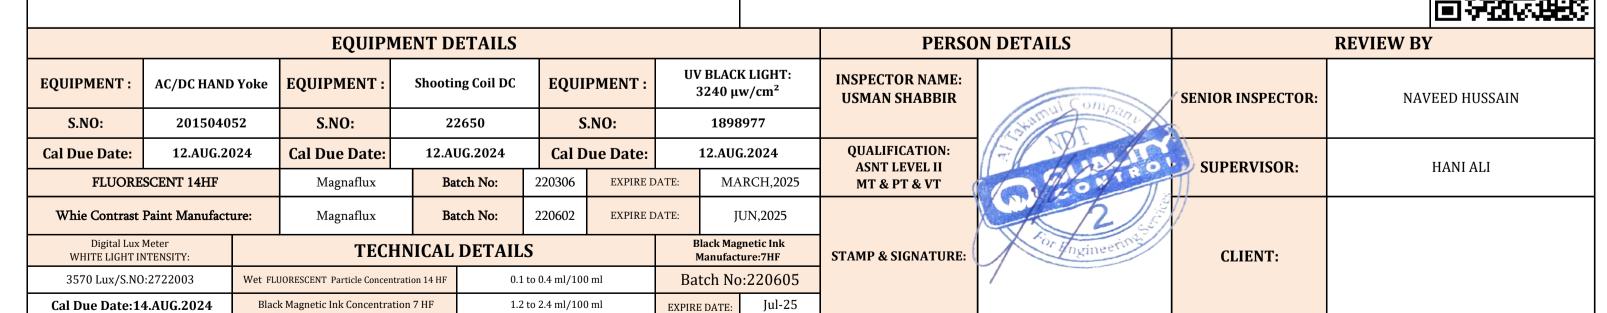

Original - Client Files

Copy - Area Office

QC/FN/MPI/065

Rev.00 DATED 07 NOV 2021

















