


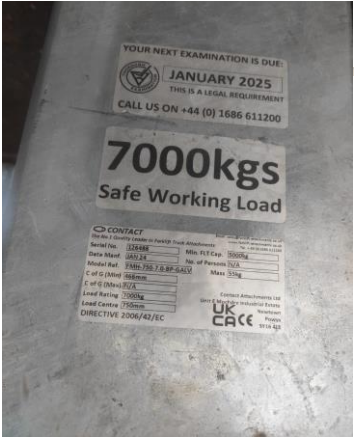


CERTIFICATION OF VISUAL, THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION

Client:	HALLIBURTON	Report No:	QC/24/HALL-0404-01A
Location:	SPERRY	Job Number:	10424
Date:	04.APRIL.2024	Next Inspection Date:	03.OCTOBER.2024
Type Of Inspection:	VISUAL , THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION	Specification:	ASTM E709 & ASTM E 1444 (2016) ASME V Article 7 (2019)
 		UNIT DESCRIPTION:	FORKLIFT TRUCK ATTACHMENT
		UNIT S/N:	126488
		UNIT SWL:	7000 KG
		INSPECTION RESULT :	
		VISUAL , THOROUGH EXAMINATION	unit fully inspected and found free from deforms, cracks, corrosion & mechanical damage
MAGNETIC PARTICLE INSPECTION	Welds & forgn areas inspected and found free from cracks and other defects		
FINAL RESULTS	unit found satisfactory and free of defects at the time of inspection		
COMMENT:			
Magnetic Particle Inspection With A/C Hand Yoke , Black & White Contrast			

EQUIPMENT DETAILS						PERSON DETAILS		REVIEW BY	
Equipment:	AC-Yoke Test Block	Equipment:	Digital Lux Meter	Equipment:	AC/DC Yoke	INSPECTOR NAME: AIZAZ FARHAT		SENIOR INSPECTOR:	ASHRAF ELSAID
S.No:	1657	S.No:	2722003	S.No:	201504052			QUALIFICATION ASNT LEVEL II MT & PT & VT	SUPERVISOR:
Cal Due Date:	12-Aug-24	Cal Due Date:	14-Aug-24	Cal Due Date:	12-Aug-24	STAMP &	CLIENT:		
Black Magnetic Ink Manufacture:	Magnaflux	Batch No:	220605	Expiry Date:	JULY.2025				
Whie Contrast Paint Manufacture:	Magnaflux	Batch No:	220602	Expiry Date:	JUN,2025				
Technical Details:	Magnetic Partical Concentration		Method		WMPT Light Intensity				

**AI TAKAMUL COMPANY FOR ENGINEERING TESTS
AND PROFESSIONAL SAFETY LIMITED**

Basra, North Rumaila, Quality Control Yard - Iraq

Tel: +9647810009138 / +9647834964657

Email: OP@qualitycontrol-iraq.com / hany.akafi@qualitycontrol-iraq.com



Date of Examination:	04/04/2024	Next Examination:	03/10/2024	Certificate No:	QC/24/HALL-0404-01A
Client Name:	Halliburton	Location:	Sperry Workshop	SN:	126488

DESCRIPTION	FORKLIFT TRUCK ATTACHMENT
SN	126488
DATE MANF	JAN 2024
MODEL REF	FMH-750-7.0-BP-GALV
C OF G (MIN)	466 MM
C OF G (MAX)	N/A
LOAD RATING	7000 KG
LOAD CENTRE	750 MM
MIN. FLT CAP.	5000 KG
NO. OF PERSONS	N/A
MASS	55 KG

