Al TAKAMUL COMPANY FOR ENGINEERING TESTS AND PROFESSIONAL SAFETY LIMITED



Basra, North Rumaila, Quality Control Yard - Iraq

CERTIFICATION OF VISUAL, THOROUGH EXAMINATON & MAGNETIC PARTICLE INSPECTION


	Client:	HALLIBURTON (TSS)	Report No:	QC/24/HALL-TSS-MAY-021
_	Location:	TSS YARD	Job Number:	QC-24/HALL-TSS-001
	Date:	Thursday, May 2, 2024	Next Inspection Date:	Friday, November 1, 2024
	Type Of Inspection:	VISUAL , THOROUGH EXAMINATION & MAGNETIC PARTICLE INSPECTION	Specification:	ASTM E709 & ASTM E 1444 (2016) ASME V Article 7 (2019)



UNIT DESCRIPTION:	TEST PLUG: 1 1/2 NPTY X 3" 206 THREAD
UNIT S/N:	490037
	INSPECTION RESULT:
VISUAL, THOROUGH EXAMINATION	VISUAL & MAGNETIC PARTICLE INSPECTION (M.P.I.) HAD BEEN DONEON THE AVAILABLE AREAS FOR THE ABOVE DESCRIPTION
MAGNETIC PARTICLE INSPECTION	Thread & Avaliable critical areas inspected and found free from cracks and other defects
FINAL RESULTS	THE ABOVE INSPECTED AREAS WAS ACCEPTED

COMMENTS:

(MPI Wet Fluorescent inspection Thread With UltraViolet Light) Magnetic Particle Inspection With A/C Hand Yoke, Black & White Contrast

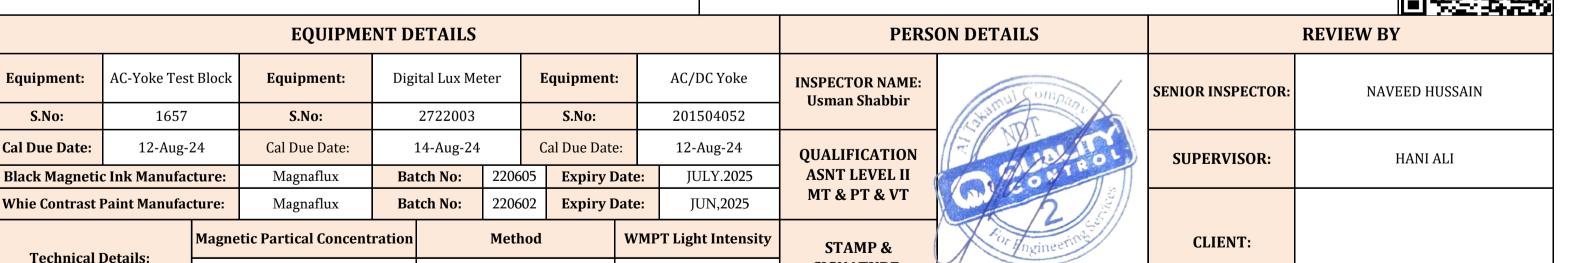

SIGNATURE:

Original - Client Files Copy - Area Office QC/FN/MPI/065 Rev.00 **DATED 07 Nov 2021**







1.2 to 2.4 ml/100 ml









Wet Magnetic Particle Testing

(WMPT)



3630 Lux
