




REPORT OF ULTRASONIC THICKNESS MEASUREMENTS

Client Name:	Daqing Drilling Company	Location:	DQ-Base	Job Number:	QC-DQ-06-24-0187
Date of Examination:	21.06.2024	Date of Report:	21.06.2024	Certificate No:	QC-DQ-06-24-0187-01
Item Description	Mud Tank			Unit S/N:	GK5S0052401

PICTURE



ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022






(Table-1) _ Measurements For Mud Tank Wall

All Measurements In MM

Tank Parts	Points	Minimum acceptable thickness (mm)	Actual Measured Thickness In (mm)							
Front	A	3 mm	6.05	5.83	5.99	6.03	5.92	5.84	5.80	5.86
	B	3 mm	5.81	5.76	5.93	5.92	5.88	5.48	5.66	5.57
Right Site	A	3 mm	6.37	6.32	6.45	6.74	6.66	6.48	6.73	6.69
	B	3 mm	6.48	6.51	6.42	6.49	6.55	6.60	6.62	6.87
	C	3 mm	6.11	6.18	6.14	6.21	6.12	6.17	6.24	6.15
	D	3 mm	6.26	6.29	6.33	6.38	6.63	6.45	6.41	6.52
	E	3 mm	6.60	6.72	6.68	6.46	6.48	6.41	6.38	6.31
Left Site	A	3 mm	6.18	6.28	6.21	6.30	6.32	6.25	6.29	6.34
	B	3 mm	6.30	6.47	6.35	6.52	6.44	6.56	6.83	6.78
	C	3 mm	6.28	6.31	6.47	6.43	6.49	6.54	6.61	6.67
	D	3 mm	6.56	6.75	6.93	6.49	6.86	6.43	6.54	6.44
	E	3 mm	6.00	6.03	6.01	6.10	6.04	6.07	6.05	6.07
End	A	3 mm	5.33	5.42	5.39	5.28	5.34	5.55	5.58	5.64
	B	3 mm	5.44	5.49	5.38	5.62	5.43	5.61	5.39	5.61
Floor	A	3 mm	7.82	7.79	7.77	7.85	7.81	7.88	7.94	8.15
	B	3 mm	6.45	6.49	6.54	6.38	6.64	6.56	6.62	6.66
	C	3 mm	7.78	7.83	7.98	7.76	7.85	7.99	8.01	8.13
	D	3 mm	7.32	7.26	7.21	7.43	7.29	7.37	7.49	7.51
	E	3 mm	8.15	8.18	8.22	8.14	8.10	8.24	8.20	8.17
UT Details										
Ref Standard	ASTM E797	Acceptance Criteria	OEM			Scanning		A-Scan		
UT Equipment Details										
Device Type	GYGNUS	Device S/N:	05058444			Frequency		2.25 MHz		
REMARK										
UT Thickness measurements has been carried out at the above description and found accepted at the time of Inspection										

ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022





REPORT OF ULTRASONIC THICKNESS MEASUREMENTS

Client Name:	Daqing Drilling Company	Location:	DQ-Base	Job Number:	QC-DQ-06-24-0187
Date of Examination:	21.06.2024	Date of Report:	21.06.2024	Certificate No:	QC-DQ-06-24-0187-02
Item Description	Mud Tank			Unit S/N:	B2

PICTURE

Front



End




Right Site



Left Site



ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025


REV: 01 Dated: 20 June 2022





(Table-2) _ Measurements For Mud Tank Wall
All Measurements In MM

Tank Parts	Points	Minimum acceptable thickness (mm)	Actual Measured Thickness In (mm)							
Front	A	3 mm	6.48	6.35	6.55	6.32	6.37	6.51	6.82	6.88
	B	3 mm	7.01	7.07	6.98	6.87	6.75	6.84	6.89	6.99
Right Site	A	3 mm	7.25	7.22	7.27	7.18	7.33	7.38	7.36	7.31
	B	3 mm	7.20	7.16	7.32	7.55	7.41	7.46	7.39	7.28
	C	3 mm	6.87	6.85	6.93	7.01	7.13	7.10	7.18	7.15
	D	3 mm	6.55	6.64	6.43	6.35	6.42	6.48	6.61	6.67
	E	3 mm	6.88	6.81	6.77	6.69	6.78	6.98	6.89	6.84
Left Site	A	3 mm	7.09	7.16	7.18	7.22	7.19	7.25	7.29	7.15
	B	3 mm	6.41	6.56	6.45	6.66	6.51	6.49	6.36	6.22
	C	3 mm	7.12	7.16	7.10	7.00	6.94	6.92	6.87	6.73
	D	3 mm	7.65	7.55	7.42	7.49	7.53	7.61	6.98	6.92
	E	3 mm	6.48	6.52	6.39	6.72	6.69	7.12	7.10	7.21
End	A	3 mm	6.32	6.41	6.48	6.41	6.45	6.72	6.92	6.88
	B	3 mm	6.22	6.26	6.32	6.54	6.41	6.53	6.69	6.47
Floor	A	3 mm	7.77	7.72	7.83	7.89	7.63	7.75	7.73	7.65
	B	3 mm	7.19	7.21	7.24	7.18	7.27	7.31	7.35	7.29
	C	3 mm	6.99	6.85	9.76	6.87	6.95	7.01	7.10	7.13
	D	3 mm	7.44	7.26	7.35	7.46	7.49	7.56	7.52	7.66
	E	3 mm	7.31	7.43	7.39	7.34	7.50	7.62	7.77	7.89
UT Details										
Ref Standard	ASTM E797	Acceptance Criteria	OEM			Scanning		A-Scan		
UT Equipment Details										
Device Type	GYGNUS	Device S/N:	05058444			Frequency		2.25 MHz		
REMARK										
UT Thickness measurements has been carried out at the above description and found accepted at the time of Inspection										

ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022

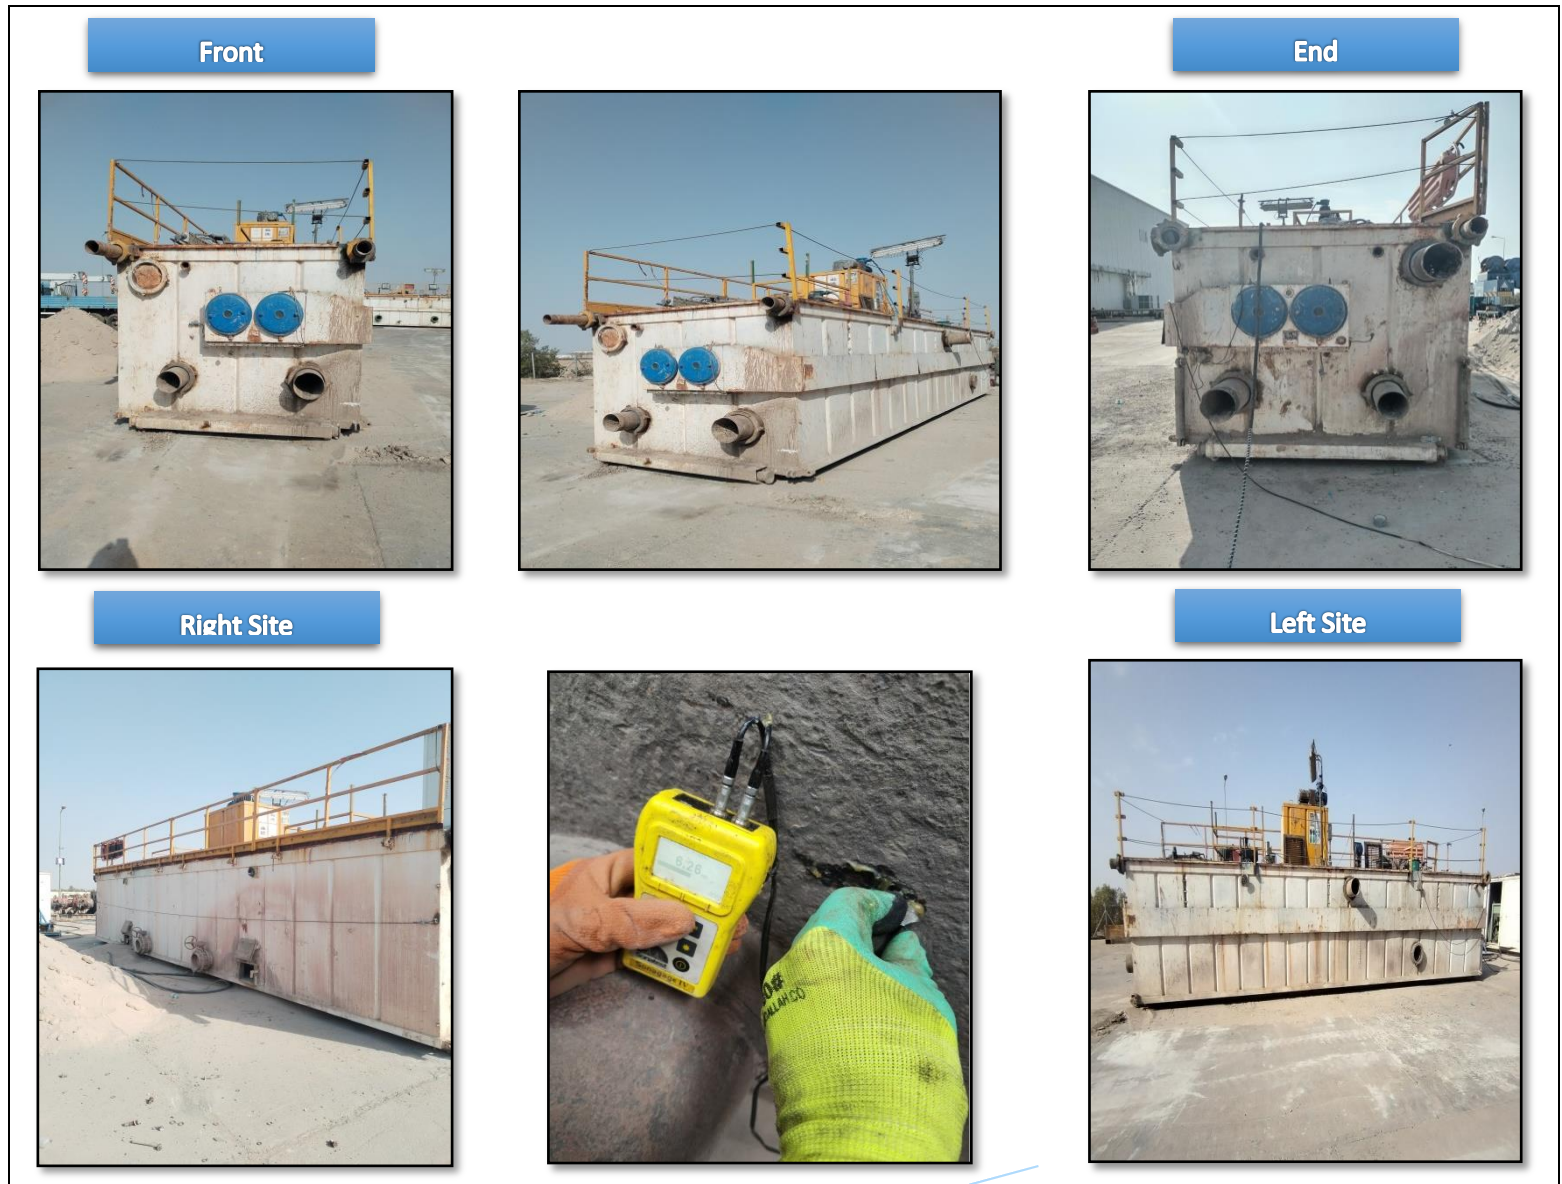





REPORT OF ULTRASONIC THICKNESS MEASUREMENTS

Client Name:	Daqing Drilling Company	Location:	DQ-Base	Job Number:	QC-DQ-06-24-0187
Date of Examination:	21.06.2024	Date of Report:	21.06.2024	Certificate No:	QC-DQ-06-24-0187-03
Item Description	Mud Tank			Unit S/N:	B3

PICTURE



ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025


REV: 01 Dated: 20 June 2022




(Table-3) _ Measurements For Mud Tank Wall

All Measurements In MM

Tank Parts	Points	Minimum acceptable thickness (mm)	Actual Measured Thickness In (mm)							
Front	A	3 mm	6.26	6.30	6.45	6.49	6.22	6.18	6.25	6.33
	B	3 mm	6.89	6.82	6.73	6.66	6.79	6.84	6.77	6.98
Right Site	A	3 mm	6.63	6.67	6.33	6.58	6.44	6.47	6.65	6.41
	B	3 mm	5.50	5.86	5.92	6.22	6.26	5.99	5.88	5.96
	C	3 mm	5.46	5.63	5.68	5.71	5.77	5.80	5.79	5.55
	D	3 mm	5.82	5.88	5.76	5.54	5.61	5.73	5.65	5.92
	E	3 mm	5.35	5.42	5.39	5.47	5.53	5.61	5.46	5.59
Left Site	A	3 mm	6.15	6.18	6.11	6.22	6.32	6.45	6.55	6.62
	B	3 mm	6.38	6.41	6.46	6.51	6.67	6.59	6.44	6.73
	C	3 mm	5.87	5.98	6.01	6.10	6.15	6.16	6.11	6.17
	D	3 mm	6.06	6.09	6.13	6.18	6.21	6.24	6.19	6.14
	E	3 mm	6.55	6.64	6.52	6.66	6.69	6.75	6.81	6.56
End	A	3 mm	6.42	6.59	6.65	6.43	6.48	6.31	6.57	6.64
	B	3 mm	6.16	6.22	6.32	6.55	6.41	6.46	6.39	6.28
Floor	A	3 mm	5.80	5.78	5.86	5.67	5.74	5.83	5.98	6.01
	B	3 mm	5.27	5.31	5.59	5.48	5.62	5.45	5.73	5.66
	C	3 mm	5.91	5.86	5.71	5.96	6.11	6.16	6.54	6.13
	D	3 mm	5.65	5.54	5.42	5.49	5.37	5.53	5.67	5.85
	E	3 mm	6.22	6.29	6.34	6.50	6.62	6.71	6.84	6.77
UT Details										
Ref Standard	ASTM E797	Acceptance Criteria	OEM			Scanning		A-Scan		
UT Equipment Details										
Device Type	GYGNUS	Device S/N:	05058444			Frequency		2.25 MHz		
REMARK										
UT Thickness measurements has been carried out at the above description and found accepted at the time of Inspection										

ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022






REPORT OF ULTRASONIC THICKNESS MEASUREMENTS

Client Name:	Daqing Drilling Company	Location:	DQ-Base	Job Number:	QC-DQ-06-24-0187
Date of Examination:	21.06.2024	Date of Report:	21.06.2024	Certificate No:	QC-DQ-06-24-0187-04
Item Description	Mud Tank			Unit S/N:	B4

PICTURE



ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025


REV: 01 Dated: 20 June 2022





(Table-4) _ Measurements For Mud Tank Wall
All Measurements In MM

Tank Parts	Points	Minimum acceptable thickness (mm)	Actual Measured Thickness In (mm)							
Front	A	3 mm	5.80	5.63	5.46	5.20	5.35	5.66	5.23	5.48
	B	3 mm	5.38	5.58	5.73	5.41	5.27	5.33	5.30	5.45
Right Site	A	3 mm	5.65	5.27	5.33	5.29	5.50	5.72	5.22	5.34
	B	3 mm	6.33	6.44	6.39	6.55	6.48	6.51	6.63	6.69
	C	3 mm	5.77	5.31	5.61	5.56	5.43	5.67	5.71	5.82
	D	3 mm	5.96	5.99	6.11	5.84	5.69	5.88	5.98	6.01
	E	3 mm	6.60	6.31	6.26	6.43	6.52	6.74	6.59	6.44
Left Site	A	3 mm	5.88	5.80	5.99	5.86	5.64	5.59	5.47	5.68
	B	3 mm	5.54	5.96	5.82	6.22	6.30	6.33	6.90	6.87
	C	3 mm	6.63	6.91	6.42	6.75	6.59	6.65	6.72	6.64
	D	3 mm	6.37	6.18	5.58	5.84	6.16	6.19	6.32	6.17
	E	3 mm	5.94	5.85	5.65	5.71	5.66	5.73	5.58	5.93
End	A	3 mm	6.18	6.29	6.13	6.16	6.33	6.22	6.32	6.25
	B	3 mm	6.65	6.72	6.78	6.66	6.53	6.41	6.81	6.91
Floor	A	3 mm	7.22	7.57	7.92	7.80	6.84	6.77	6.65	6.82
	B	3 mm	6.48	6.73	6.26	6.52	6.63	6.45	6.67	6.77
	C	3 mm	7.15	7.19	7.11	7.07	7.22	7.17	7.25	7.31
	D	3 mm	6.25	6.18	6.33	6.80	5.98	6.01	6.14	6.22
	E	3 mm	6.77	6.54	6.86	6.69	6.92	6.75	6.63	7.10
UT Details										
Ref Standard	ASTM E797	Acceptance Criteria	OEM			Scanning		A-Scan		
UT Equipment Details										
Device Type	GYGNUS	Device S/N:	05058444			Frequency		2.25 MHz		
REMARK										
UT Thickness measurements has been carried out at the above description and found accepted at the time of Inspection										

ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022





REPORT OF ULTRASONIC THICKNESS MEASUREMENTS

Client Name:	Daqing Drilling Company	Location:	DQ-Base	Job Number:	QC-DQ-06-24-0187
Date of Examination:	21.06.2024	Date of Report:	21.06.2024	Certificate No:	QC-DQ-06-24-0187-05
Item Description	Mud Tank			Unit S/N:	B5

PICTURE

Front



End




Right Site



Left Site



ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025


REV: 01 Dated: 20 June 2022





(Table-5) _ Measurements For Mud Tank Wall
All Measurements In MM

Tank Parts	Points	Minimum acceptable thickness (mm)	Actual Measured Thickness In (mm)							
Front	A	3 mm	5.96	5.88	5.84	5.76	5.82	5.77	5.94	5.97
	B	3 mm	5.99	5.92	6.00	6.01	6.07	6.10	6.14	6.11
Right Site	A	3 mm	6.63	6.51	6.42	6.38	6.27	6.33	6.41	6.53
	B	3 mm	6.75	6.64	6.57	6.69	6.71	6.48	6.52	6.56
	C	3 mm	6.79	6.67	6.63	6.58	6.45	6.55	6.61	6.75
	D	3 mm	6.13	6.16	6.22	6.24	6.19	6.28	6.32	6.38
	E	3 mm	6.85	6.79	6.73	6.68	6.64	6.59	6.61	6.51
Left Site	A	3 mm	6.48	6.55	6.67	6.56	6.45	6.38	6.42	6.54
	B	3 mm	6.62	6.71	6.79	6.83	6.97	7.01	7.11	7.15
	C	3 mm	7.23	7.27	7.36	7.31	7.29	7.43	7.48	7.57
	D	3 mm	6.85	6.79	6.98	7.00	7.13	7.18	7.22	7.26
	E	3 mm	7.42	7.46	7.52	7.63	7.76	7.83	7.89	7.95
End	A	3 mm	6.20	6.19	6.15	6.17	6.13	6.21	6.25	6.32
	B	3 mm	5.86	5.79	5.72	5.84	5.78	5.86	5.98	6.01
Floor	A	3 mm	8.33	8.29	8.24	8.36	8.45	8.57	8.61	8.68
	B	3 mm	7.89	7.92	7.85	7.81	7.78	7.77	7.96	8.01
	C	3 mm	7.44	7.31	7.26	7.45	7.52	7.74	7.59	7.62
	D	3 mm	7.33	7.47	7.35	7.52	7.44	7.78	7.83	7.56
	E	3 mm	7.65	7.59	7.61	7.43	7.45	7.31	7.57	7.48
UT Details										
Ref Standard	ASTM E797	Acceptance Criteria	OEM			Scanning		A-Scan		
UT Equipment Details										
Device Type	GYGNUS	Device S/N:	05058444			Frequency		2.25 MHz		
REMARK										
UT Thickness measurements has been carried out at the above description and found accepted at the time of Inspection										

ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022





REPORT OF ULTRASONIC THICKNESS MEASUREMENTS

Client Name:	Daqing Drilling Company	Location:	DQ-Base	Job Number:	QC-DQ-06-24-0187
Date of Examination:	21.06.2024	Date of Report:	21.06.2024	Certificate No:	QC-DQ-06-24-0187-06
Item Description	Mud Tank			Unit S/N:	B6

PICTURE

Front



End




Right Site



Left Site



ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025


REV: 01 Dated: 20 June 2022





(Table-6) _ Measurements For Mud Tank Wall
All Measurements In MM

Tank Parts	Points	Minimum acceptable thickness (mm)	Actual Measured Thickness In (mm)							
Front	A	3 mm	5.54	5.27	5.94	5.96	5.42	5.58	5.39	5.50
	B	3 mm	6.82	6.63	6.90	6.84	6.78	6.69	6.72	6.66
Right Site	A	3 mm	6.97	6.86	7.18	7.31	7.35	7.42	7.48	7.65
	B	3 mm	6.26	6.16	6.10	6.15	6.22	6.18	6.45	6.51
	C	3 mm	6.07	6.11	6.19	6.22	6.14	6.28	6.32	6.43
	D	3 mm	6.33	6.41	6.73	6.94	6.69	6.86	6.77	6.67
	E	3 mm	6.11	6.26	6.31	6.52	6.37	6.45	6.82	6.86
Left Site	A	3 mm	6.30	6.33	6.67	6.52	6.45	6.49	6.55	6.64
	B	3 mm	6.52	6.41	6.37	6.35	6.44	6.54	6.58	6.63
	C	3 mm	5.88	5.85	5.98	6.09	6.14	6.17	6.11	6.15
	D	3 mm	6.12	6.35	6.71	6.94	6.76	6.55	6.64	6.57
	E	3 mm	6.03	5.99	6.11	6.18	6.15	6.25	6.22	6.34
End	A	3 mm	6.92	7.27	7.20	7.39	7.24	7.29	7.36	7.41
	B	3 mm	6.88	6.79	6.75	6.98	7.04	7.14	7.22	7.33
Floor	A	3 mm	7.61	7.46	7.50	7.67	7.82	7.88	7.97	7.84
	B	3 mm	6.29	6.33	6.87	6.79	6.98	7.12	7.19	7.25
	C	3 mm	7.61	7.45	7.39	7.53	7.57	7.64	7.77	7.82
	D	3 mm	7.55	7.59	7.62	7.67	7.73	7.52	7.61	7.68
	E	3 mm	7.29	7.35	7.47	7.42	7.56	7.61	7.75	7.77
UT Details										
Ref Standard	ASTM E797	Acceptance Criteria	OEM			Scanning		A-Scan		
UT Equipment Details										
Device Type	GYGNUS	Device S/N:	05058444			Frequency		2.25 MHz		
REMARK										
UT Thickness measurements has been carried out at the above description and found accepted at the time of Inspection										

ASNT Level II Inspector Name:	Signature & Stamp:	Date of Next Through Examination:
Jaafar Badr		20-06.2025

REV: 01 Dated: 20 June 2022

