




Online Traceability



AL TAKAMUL COMPANY FOR ENGINEERING SERVICES
QUALITY CONTROL - IRAQ

Visual Through Examination & Magnetic Particles Examination Certificate

Client	DAQING DRILLING COMPANY	Location	DQ RIG 022		
Date of Examination:	21.Dec.2024	Certificate No:	QC-DQ-12-24-0249/78		
Date of Next Through Examination:	20.Jun.2025	Job Order Number:	QC-YB-240135		
Description of the Examined Equipment		Serial Number	Result	COLOR CODE	
T- Wall Pad Eyes		TW-002	Pass	ORANGE	
Pad Eyes S/N:	W5, W6, W7, W8				
PAD EYES DIMENSION	PIN HOLE	THICKNESS	LENGTH PASS	HIGHT	SWL:
	39 MM	20 MM	128 MM	98 MM	4 TON

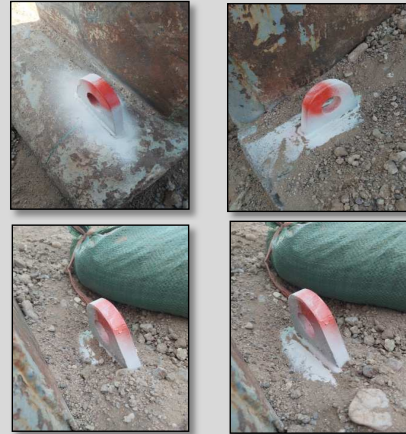

INSPECTION RESULT :

VISUAL THOROUGH EXAMINATION	Unit inspected and found free from deforms, cracks, corrosion & mechanical damage
MAGNETIC PARTICLE INSPECTION	Welds & forgn areas inspected and found free from cracks and other defects
FINAL RESULTS	Unit found satisfactory and free of defects at the time of inspection

NDT Equipment Details

Standard	ASTM E709	Viewing Condition:	Colored Media	Method:	WET
AC/DC YOKE	Permanent	Serial No:	201504048	Due Date:	25-Aug-24
White Contrast	WCP-2	Batch No:	008A009	Due Date:	Apr-26
Black Ink	7HF	Batch No:	008A103	Due Date:	Jul-25

ASNT Level II Inspector Name:	Authenticating This Report:	Signature & Stamp:	Review Signature & Stamp:
Jaafar Badr	Ashraf Alsaad		

