




Online Traceability



AL TAKAMUL COMPANY FOR ENGINEERING SERVICES  
QUALITY CONTROL - IRAQ

**Visual Through Examination & Magnetic Particles Examination Certificate**

Client	DAQING DRILLING COMPANY	Location	DQ RIG 022		
Date of Examination:	21.Dec.2024	Certificate No:	QC-DQ-12-24-0249/91		
Date of Next Through Examination:	20.Jun.2025	Job Order Number:	QC-YB-240135		
Description of the Examined Equipment		Serial Number	Result	COLOR CODE	
Security Tower pad Eyes		SC-01	Pass	ORANGE	
Pad Eyes S/N:	S17, S18, S19, S20, S21, S22				
PAD EYES DIMENSION	PIN HOLE	THICKNESS	LENGTH PASS	HIGHT	SWL:
	39 MM	20 MM	110 MM	105 MM	4 TON

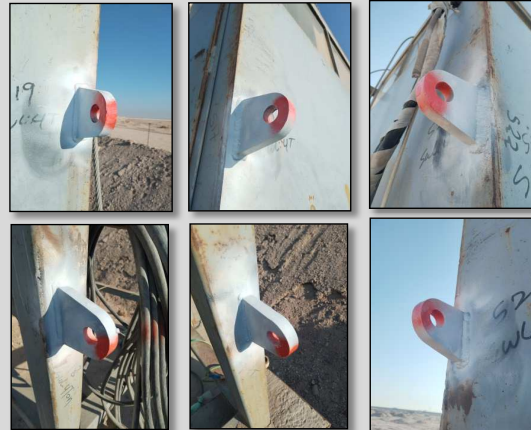

**INSPECTION RESULT :**

VISUAL THOROUGH EXAMINATION	Unit inspected and found free from deforms, cracks, corrosion & mechanical damage
MAGNETIC PARTICLE INSPECTION	Welds & forgn areas inspected and found free from cracks and other defects
FINAL RESULTS	Unit found satisfactory and free of defects at the time of inspection

**NDT Equipment Details**

Standard	ASTM E709	Viewing Condition:	Colored Media	Method:	WET
AC/DC YOKE	Permanent	Serial No:	201504048	Due Date:	25-Aug-24
White Contrast	WCP-2	Batch No:	008A009	Due Date:	Apr-26
Black Ink	7HF	Batch No:	008A103	Due Date:	Jul-25

ASNT Level II Inspector Name:	Authenticating This Report:	Signature & Stamp:	Review Signature & Stamp:
Jaafar Badr	Ashraf Alsaad		

