





## Visual & Magnetic Particles Examination Report

Client:	DAQING DRILLING COMPANY	Certificate no:	QC-B-05-25-0331-3/04
Location:	DQ RIG 012	Job Order No:	QC-B-05-25-0331
Date of Examination:	09-June-2025	Next Inspection Due:	08-Dec-2025
<b>Unit Serial Number</b>	<b>Description of the examined equipment</b>		<b>Result</b>
222287	Rig Floor Air Winch Welding Area		Accept
SWL	50 KN		

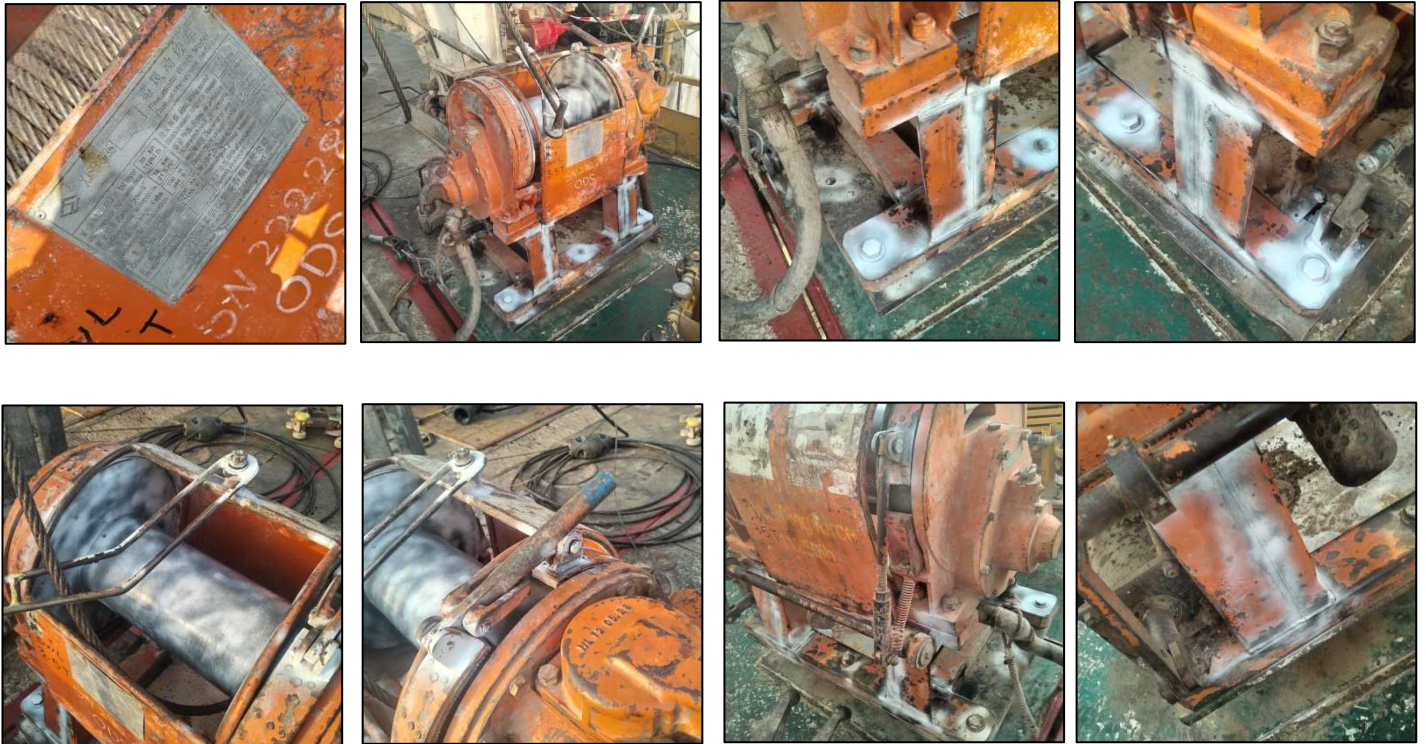

NDT Equipment Details					
Standard	ASTM E 709	Viewing Condition:	Colored Media	Method	WET
Yoke	Permanent	Serial No:	PY-10	Due Date	10. Nov.2025
White Contrast	WCP-2	Batch No:	008A009	Due Date	April.2026
Black Ink	7HF	Batch No:	008A103	Due Date	Jun.2026
NDT procedure					
Visual and MPI were carried out for the above description and found free of surface defects at the time of inspection					
Identification of any part found to have a defect and a description of the defect: None					
Particulars of any repair, renewal, or alteration required to remedy the defect identified above: None					
All MPI was performed per OEM's instructions, and OEM did the measurements.					

LEEA & ASNT Level II Inspector Name:	Signature:	Authenticating This Report:	
Khaled Mahmoud		Mohammed Abdulla	
