


UT Inspection Certificate

Client:	SLB Basra	Report No:	QC-SLB-25185-27
Work Location:	TESTING WORK SHOP	Date Of Inspection:	16/Jul/2025
Reference:	ASTM E709 & ASTM E797	Next Inspection Date:	15/Jul/2026

Specification:	☐ API ☐ DS1 ☒ Customer spec ☐ Other	
Inspection method:	☐ MPI ☐ Wet ☐ Dry ☐ Dye Penetrant ☐ VTI ☒ Ultrasonic wall thickness spot test ☐ Others	
Equipment used:	☐ UVB light ☐ AC yoke ☐ DC coil ☒ Ultrasonic T.G. ☐ Other	

Material Inspected:	AIR COMPRESSOR
---------------------	-----------------------

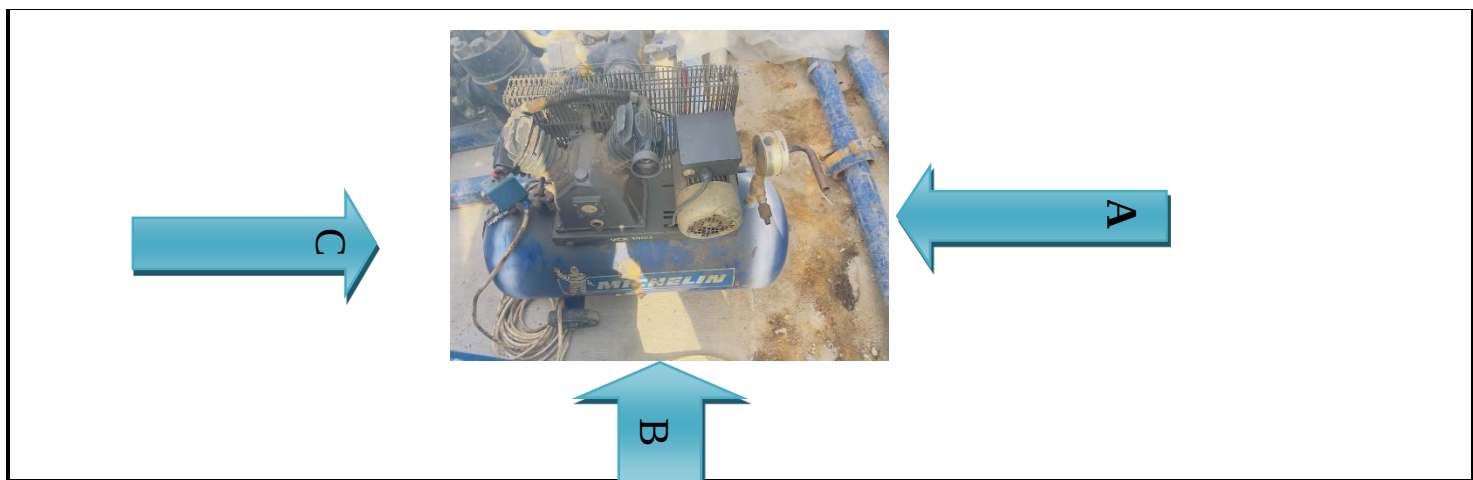

Serial No.	Ultrasonic Thickness Measurements				Minimum Thickness
TS-CO-011					
Location A	3.88 mm	3.88 mm	3.88 mm	3.86 mm	2.45 mm
Location B	3.88 mm	3.80 mm	3.86 mm	3.88 mm	2.40 mm
Location C	3.88 mm	3.90 mm	3.88 mm	3.80 mm	2.45 mm

Inspection Evaluation:	U.T	During All The Reading Are Within The Tolerance And Accepted Min Thickness According to Schlumberger Reference.
Inspection Evaluation:	MPI	unit found satisfactory and free of defects at the time of inspection

Inspection Equipment Details:	U.T Wall Thickness :	Serial Number	5202746	EXPIRY :
	AC/DC YOKE :	SN: 20150Y048	Cal Due Date:	24-Aug-2025

SUPERVISOR	M-TAREK	Inspection Engineer:	Bilal Akram
------------	---------	----------------------	-------------

