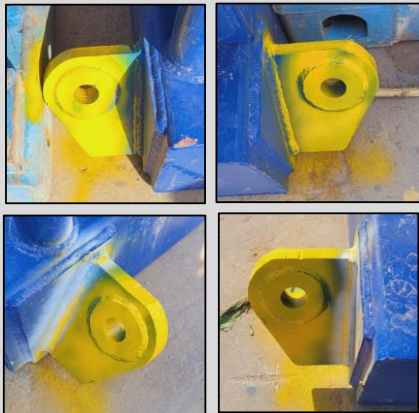


		Online Traceability		AI TAKAMUL COMPANY FOR ENGINEERING TESTS AND PROFESSIONAL SAFETY LIMITED QUALITY CONTROL-IRAQ	
Visual Through Examination & Magnetic Particles Examination Report					
Client	SLB Basra		Location		Artificial Lift BackYard
Date of Examination:	23/Sep/2025		Certificate No:		QC-SLB/25245-31
Date of Next Through Examination:	22/Mar/2026		Job Order Number:		QC-SLB/25245
Description of the Examined Equipment			Serial Number		Result
Hydraulic Field Spooler with Fairlead Capacity: 15 Ton			6463		Pass
HOLE DIMENSION	PIN HOLE	THICKNESS	LENGTH PASS	HIGHT	SWL
	30 mm	35 mm	165 mm	120 mm	6 Ton
 					
INSPECTION RESULT :					
VISUAL THOROUGH EXAMINATION		Unit inspected and found free from deforms, cracks, corrosion & mechanical damage			
MAGNETIC PARTICLE INSPECTION		Welds & forgn areas inspected and found free from cracks and other defects			
FINAL RESULTS		Unit found satisfactory and free of defects at the time of inspection			
NDT Equipment Details					
Standard	ASTM E709	Viewing Condition:	Colored Media	Method:	WET
AC/DC YOKE	Permanent	Serial No:	201504048	Due Date:	22-Feb-26
White Contrast	WCP-2	Batch No:	008A009	Due Date:	Feb-28
Black Ink	7HF	Batch No:	008A103	Due Date:	Jun-26
ASNT Level II Inspector Name:		Authenticating This Report:		Signature & Stamp:	
Moohamed Abdallah		Ashraf Elsaad			
        					
QC-QA-MT-047 Rev.00 01Date Jul-2024.					
