


MPI & UT. Wall Thickness Gauging Inspection Certificate

Client:	SLB BASRA	Report No:	QC-SLB-25264-26
Work Location:	COIL TUBING	Date of Inspection:	31/Oct/2025
Reference:	ASTM E 797 & ASTM E 709	Next Inspection Date:	30/Apr/2026

Specification:	☐ API ☐ DS1 ☒ Customer spec ☐ Other		
Inspection method :	☒ MPI ☐ Wet ☐ Dry ☐ Dye Penetrant ☐ VTI ☐ Dimensional check ☒ Ultrasonic wall thickness spot test ☐ Others		
Equipment used :	☐ UVB light ☐ AC yoke ☐ DC coil ☒ Ultrasonic T.G. ☐ Other		

Material Inspected:	RAISER 101-31180 6 FT / 4" (10K)
---------------------	---

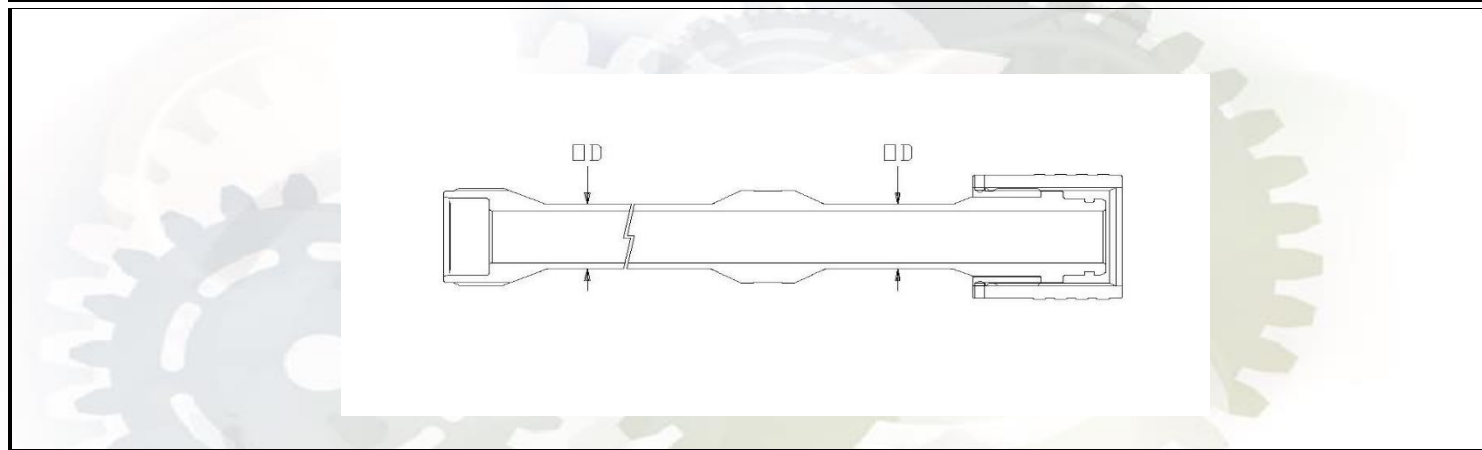

Serial No.	Ultrasonic Thickness Measurements				Minimum Thickness
	A		B		
101-31180	0.823 in	0.829 in	0.825 in	0.828 in	Accept by customer

Inspection Evaluation:	U.T	During The Time of Inspection, All The Readings Are Within The Tolerance and Accepted By SLB Requirements:
	MPI	The Above Mentioned Item Was Inspected by MPI and Found Free of Defects (No Cracks) Found At The Time of Inspection:

Inspection Equipment Details:	U.T Wall Thickness	Serial No	5202746	Cal Date	22/Feb/2026
-------------------------------	--------------------	-----------	---------	----------	-------------

Min = Minimal W.T	TE=Thread Elongation	CO= Corrosion	W = Washout	M = Flat spot / Mash	SD= shoulder Damage
-------------------	----------------------	---------------	-------------	----------------------	---------------------

SUPERVISOR:	M.TAREK	Inspection Engineer:	
-------------	----------------	----------------------	--

